CITY OF BREMERTON WASTEWATER COMPREHENSIVE PLAN UPDATE - SCHEDULE FOR DELIVERY, LAST UPDATED 12/15/24

ID	Task Mode	Task Name	Duration	Start	Finish
1					
2					
3		Update Individual section and TMs	101 days	Tue 10/1/24	Tue 2/18/25
4		Submit compiled 90% draft to City	0 days	Tue 2/18/25	Tue 2/18/25
5		**SEPA Determination**	**47 days**	**Wed 2/19/25**	**Thu 4/24/25**
6		Complete and Submit Application to DCD (checklist and 90% draft)	5 days	Wed 2/19/25	Tue 2/25/25
7		DCD Review	22 days	Wed 2/26/25	Thu 3/27/25
8		Ad and post for Public Comment	10 days	Fri 3/28/25	Thu 4/10/25
9		Issue Determination	10 days	Fri 4/11/25	Thu 4/24/25
10		**Public Review**	**40 days**	**Wed 2/19/25**	**Tue 4/15/25**
11		Upload 90% draft to project website	2 days	Wed 2/19/25	Thu 2/20/25
12		Public Comment	20 days	Wed 2/19/25	Tue 3/18/25
13		Revisions by City	15 days	Wed 3/19/25	Tue 4/8/25
14		Upload revised document on project website	5 days	Wed 4/9/25	Tue 4/15/25
15		**Ecology Review**	**94 days**	**Tue 2/18/25**	**Mon 6/30/25**
16		Prepare and submit draft document to Ecology	0 days	Tue 2/18/25	Tue 2/18/25
17		Ecology review	66 days	Wed 2/19/25	Wed 5/21/25
18		Revisions by City	15 days	Thu 5/22/25	Wed 6/11/25
19		Send back to Ecology	3 days	Thu 6/12/25	Mon 6/16/25
20		Approval by Ecology	10 days	Tue 6/17/25	Mon 6/30/25
21		**Council Approval**	**17 days**	**Tue 7/1/25**	**Wed 7/23/25**
22		Schedule with Council	12 days	Tue 7/1/25	Wed 7/16/25
23		Study Session and Full Council	5 days	Thu 7/17/25	Wed 7/23/25
24		Document Final and Approved	0 days	Wed 7/23/25	Wed 7/23/25
25		**Update City Services Section 4.6**	**27 days**	**Mon 2/10/25**	**Wed 3/19/25**
26		Submit updated service section to DC	0 days	Mon 2/10/25	Mon 2/10/25
27		Provide compiled WWCP 90% draft to DCD	0 days	Tue 2/18/25	Tue 2/18/25
28		Planning Commission Meeting	0 days	Mon 2/24/25	Mon 2/24/25
29		City Council Study Session	0 days	Wed 3/12/25	Wed 3/12/25
30		City Council Public Meeting	0 days	Wed 3/19/25	Wed 3/19/25

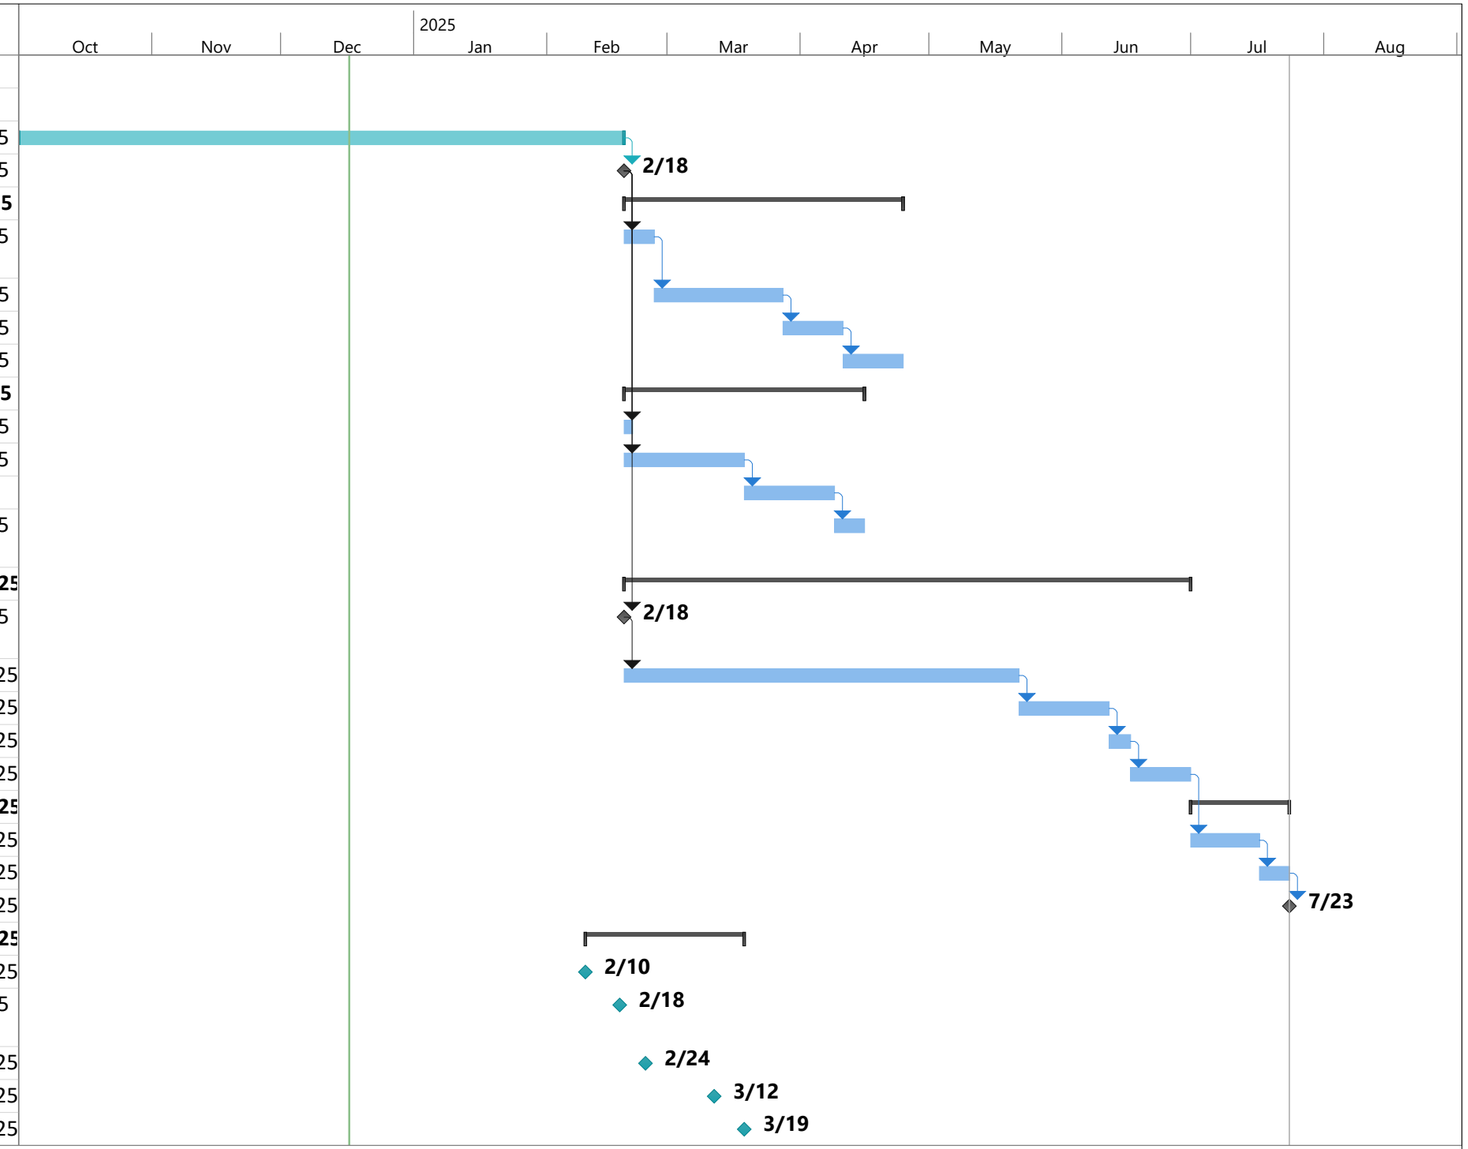

Project: WWCP Proposed comp
Date: Tue 12/17/24

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
